


## APPENDIX: Completed and Near-Term Actions

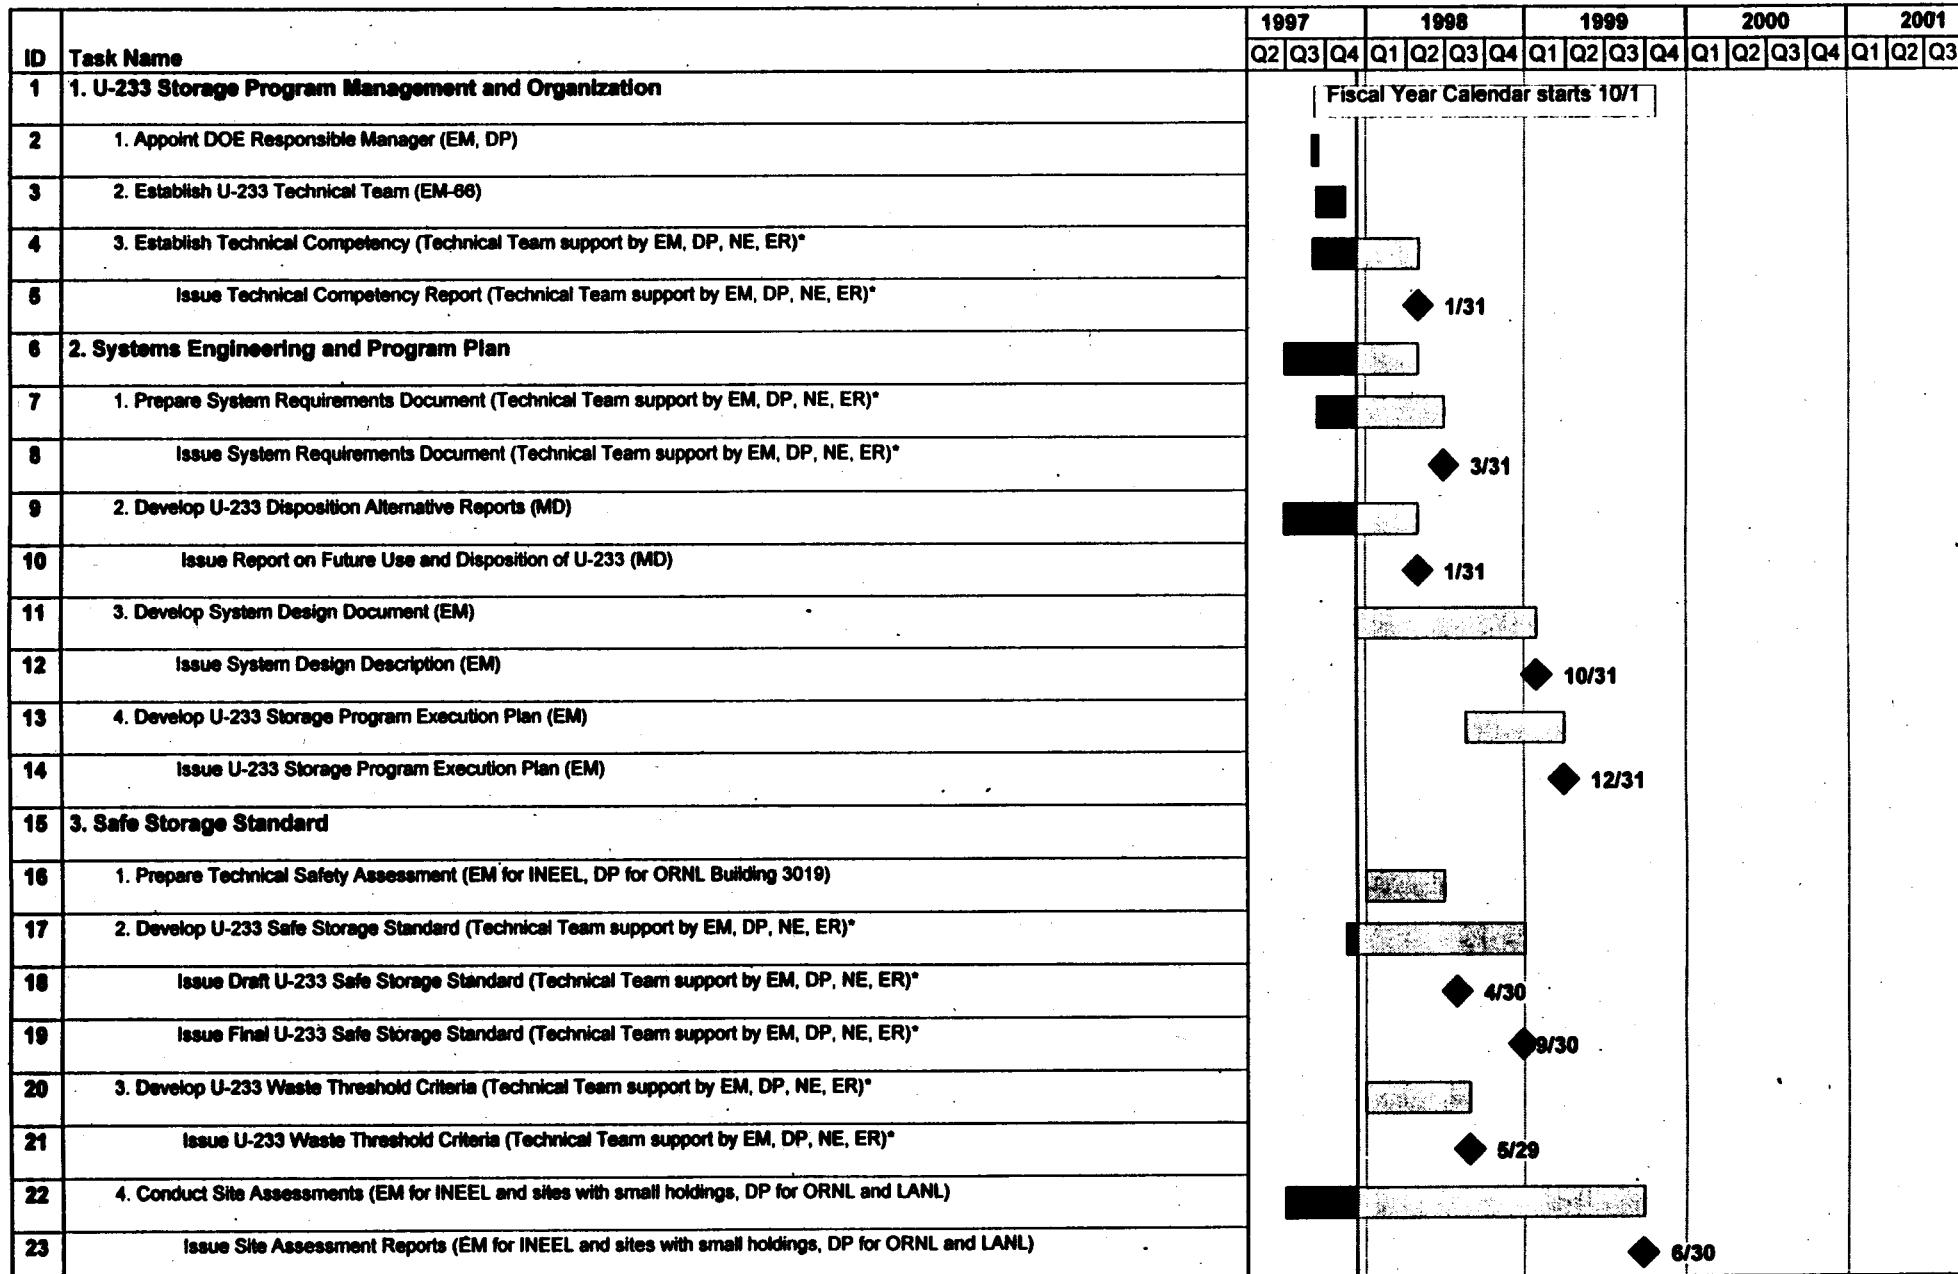

\* EM-66 provides management, coordination, and support services for the technical team, while other offices (NE, DP, MD, ER) provide federal staff consistent with the workload in the schedule.

## APPENDIX: Completed and Near-Term Actions

ID	Task Name	1997			1998			1999			2000			2001		
		Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
24	4. Site Specific Actions															
25	4.1 Oak Ridge National Laboratory - Building 3019 (DP has responsibility)															
26	1. Conduct Smear Sampling of Storage Vaults Off-Gas Piping															
27	2. Perform Trend Analysis of Off-Gas and Survey Data															
28	3. Perform Gas and Smear Sampling of 50% of Storage Vaults															
29	4. Develop Package Inspection Plan															
30	5. Review Hazards and Risks of P-24 Tank Transfer															
31	6. Develop P-24 Stabilization Plan and Flowsheet Testing															
32	7. Conduct Natural Phenomena Hazards Analysis															
33	8. Assess Ventilation System Requirements															
34	9. Update Facility Authorization Basis															
35	10. Consolidate U-233 from Small Holdings Sites															
36	11. Procure Hot Cells for Inspection and Repacking															
37	12. Install Hot Cells and Equipment and Prepare for Operations															
38	13. Complete Glove Box Off-Gas System Upgrades															
39	4.2 Idaho National Engineering and Environmental Laboratory (EM has responsibility)															
40	4.2.1 Radioactive Waste Management Center															
41	1. Radiograph 12 Drums in ASB-II (complete)															
42	2. Relocate 12 Drums from ASB-II to ILTSF (complete)															
43	3. Inspect and Repackage 63 Drums at ILTSF															
44	4. Relocate 65 Drums from ILTSF to Enclosed Storage															
45	4.2.2 Chemical Processing Plant - 749															
46	1. Analyze Gas Samples from 50% of LWBR Vaults															

Note: Any near-term actions that extend beyond 12/31/98 will be incorporated into the PEP.

## APPENDIX: Completed and Near-Term Actions

ID	Task Name	1997			1998			1999			2000			2001		
		Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
47	2. Inspect (Video) LWBR Dry Storage Vaults															
48	4.3 Los Alamos National Laboratory (DP)															
49	1. Complete streaming study to prepare CMR floor hole storage array															
50	2. Radiograph U-233 material currently located at TA-18 hillside vault															
51	3. Complete USQD for storage, consolidation, and stabilization of material in CMR building															
52	4. Transport excess hillside vault material to CMR															
53	4.4 Other Sites															
54	1. Identify Excess U-233 Materials for consolidation (EM, DP, NE for their respective holdings)															
55	2. Ship excess U-233 Materials to ORNL (EM, DP, NE for their respective holdings)															

\* EM-66 provides management, coordination, and support services for the technical team, while other offices (NE, DP, MD, ER) provide federal staff consistent with the workload in the schedule.
